BRUHAT BANGALORE MAHANAGARA PALIKE

Improvements to roads and drains at Doddabettahalli Layout, Rajeevanagara, Chikkabettahalli Surrounding area, Ananthapura surrounding area, Chitra Layout, Pulakeshinagar Layout, Jothinagar Surrounding area, Basavalingappanagara, Ananthapura Colony, Tanary road Attur Colony and Halenagara Village Colony in Ward No.03 Attur

Sl No	Description of Work	Unit	BOQ Qty	Executed Qty	% of Work Completed
1	KSRRB 300 - Excavation for road, drains and similar works KSRRB 300-1. Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2 meters and an average lift upto 0.5 m, excavated surface leveled and sides neatly dressed, the disposed earth to be leveled neatly after breaking of clods complete as per specifications including all lead and lifts and as per the direction of engineer in charge	Cum	13540.74	13540.52	100.00
2	KSRRB M2100-10. Providing and laying Plain cement concrete of mix 1:3:6 with OPC @ 220kgs, with crushed 40mm and down size graded granite metal coarse aggregates @0.89cum and fine aggregates @ 0.46cum, in foundation mechanically mixed, placed in foundation and compacted by vibration including curing for 14 days including cost of all materials, labour, HOM curing, form works, scaffolding and centering complete as per specifications including all lead and lifts and as per the direction of engineer in charge	Cum	2402.00	2401.59	99.98
3	Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300 kgs. With 20mm and sown size granite metal course aggregates at 0.69 cum and fine aggregates at 0.43 cum machine mixed, well compcted for walls and bottom including centring shuttering cost of material HOM of machinary curing etc., complete execluding cost of steel as per MORTH specification no. 1500, 1700, 2200 including cost of material labour HOM complete as per specifications including all lead and lifts and as per	Cum	3625.97	3625.89	100.00
4	KSRRB - M2300-14: Providing TMT steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, palcing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining memebrs wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM of machinery complete as per specifications including all lead and lifts and as per the direction of engineer in charge	Tn	222.13	222.13	100.00
5	Providing and fixing RCC precast cover slab of 100mm thick for drain in cement concrete 1:1.5:3 using graded granite jelly 20mm and down size with steel reinforcement, including form work, lift charges, curing and concrete finished surfaces on both sides etc, complete and as per drawing including all lead and lifts and as per the direction of engineer in charge	Sqm	7764.02	7611.92	98.04
6	Providing and fixing RCC precast cover slab of 250mm thick made out of CC 1:2:4 and jelly 20mm and down size with steel reinforcement, including form work, lift charges, curing and concrete finished surfaces on both sides etc, complete and as per drawing a including all lead and lifts and as per the direction of engineer in charge	Sqm	310.71	310.62	99.97

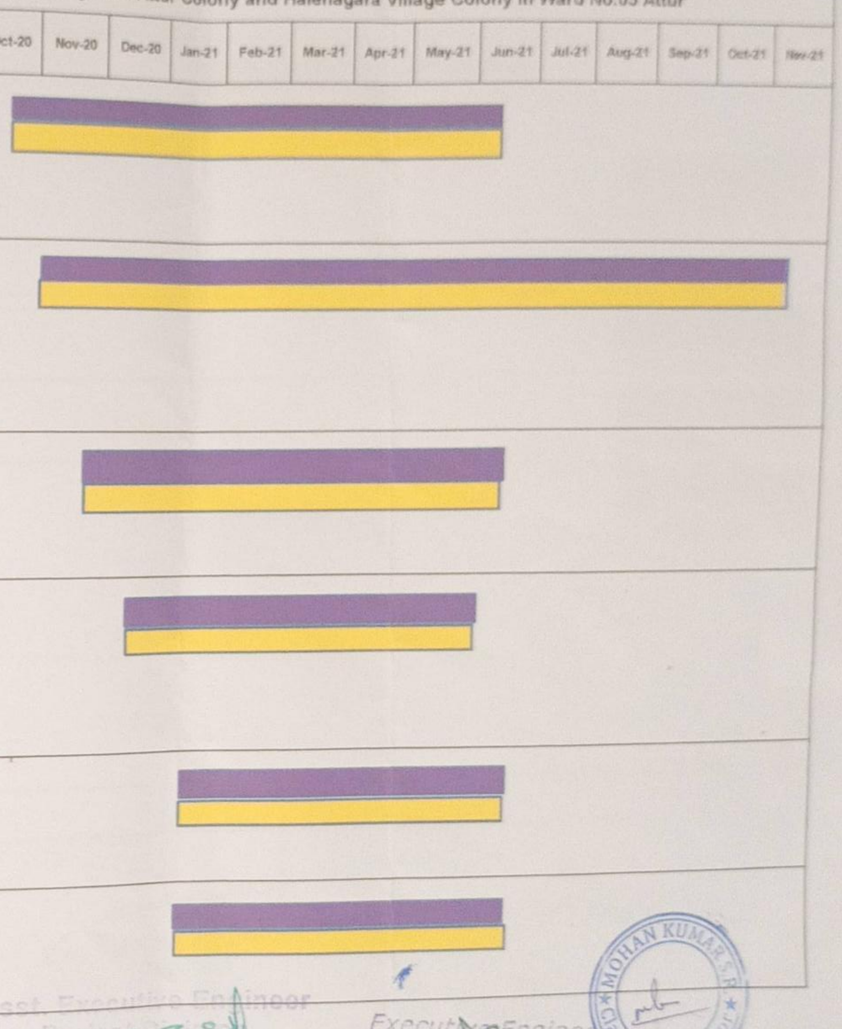

AE

Asst. Executive Engineer
Yelahanka Zone
BBMP, Bangalore - 92

Executive Engineer
Yelahanka Zone

MOHAN KUMAR S R
Class-1 Contractor

BRUHAT BANGALORE MAHANAGARA PALIKE

Scanned by TapScanner

	-1.6 ; Providing and laying in position plain cement concrete of 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregtes @ 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM curing complete as per specifications.	Cum	88.16	88.12	99.96	
8	Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour charges of machinery, loading and unloading, lead	Nos	9809.00	9809.00	100.00	
10	KSRRB M300-14. Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete as per specifications including all lead and lifts and as per the direction of engineer in charge	Cum	1231.73	1231.56	99.99	
11	KSRRB 300-58. Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per specifications.	Sqm	4105.75	4105.20	99.99	
12	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site, spreading in uniform layers with motor	Cum	615.86	615.78	99.99	
13	Constructing un-reinforced, plain cement concrete for pavements using Grade concrete M30 with OPC at 360 kg/cum and coarse aggregate 0.69cum, fine aggregate 0.46cum. over a prepared base with OPC coarse aggregate at 0.69 cum, fine aggregates at 0.46 cum,Coarse and fine aggregate conforming to IS:383-2016, with Superplastizer at 3 lts conforming to IS 9103-2008. mixed in a concrete mixer of not less than 0.6 cum capacity and appropriate weigh batcher as per approved mix design, laid in approved fixed side form work (steel channel, laying and fixing of 125 micron thick polythene film, wedges, steel plates including levelling the form work as per drawing). & Spreading the concrete with shovels, rackers compacted using needle, screed and plate vibrator and finished with floaters in a continuous operation including provision of contraction, expansion, construction and longitudinal joints,including groove cutting charges, joint filler, separation membrane of impermiable plastic sheet of 125 micron, sealant primer, joint sealant, admixtures as approved, curing compound, finishing to lines and grades, textured with texturing machine, and curing including cost of all materials, labour,hire	Cum	615.86	615.78	99.99	

= Planned %

= Executed %

AE

Asst. Executive Engineer
Project Division
Zone

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore

Class-1 Contractor

Scanned by TapScanner
